


CCC Handover – Summary of progress

Number of asset packages * #20	Total km of CCC Roads 30.5km	Number adopted #16	km Adopted 26.1km	Adoptions in CCC notice period ** #0	Final Inspections Complete #1	Awaiting works completion #3
--	--	------------------------------	-----------------------------	--	---	--

* Excludes PROW & some NMU Routes

** Some assets in adoption delay

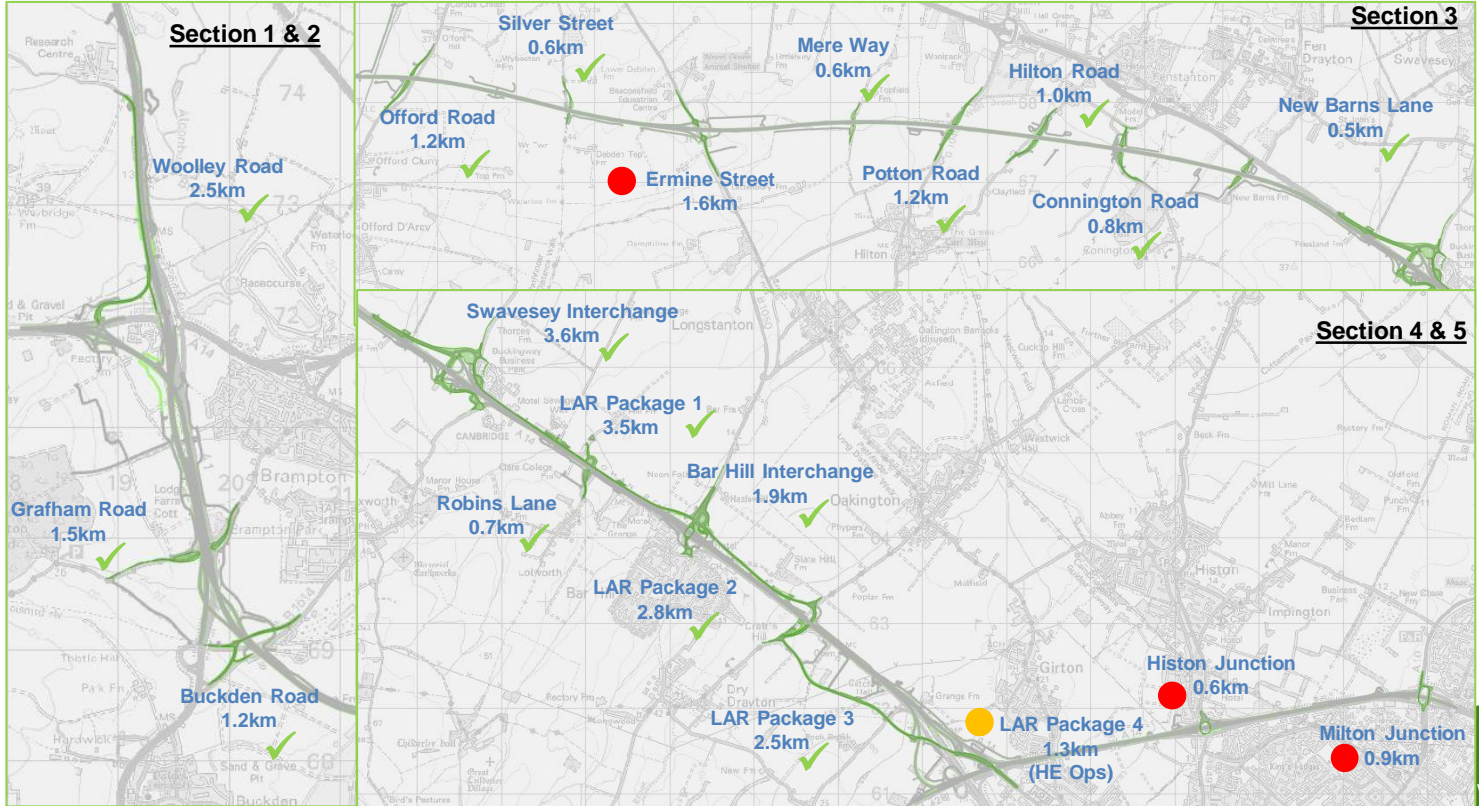

Symbol Key re, adoption status

- ✓ Denotes asset adopted
- Asset adoption request issued and on track
- Asset adoption request issued but delayed **
- Asset not yet complete / request to adopt not issued as DOWLS underway

** Note, see next slide for details on assets with adoption delay

Handover

West

Package	Forecast / Actual *	Status
A14 Mainline	09/12/2019	Adopted - Complete
A1(M) - RMS	Feb 2021	Works outstanding (gantry vrs, signs)
Silver Street	20/08/2019	Adopted - Complete
Offord Road	03/08/2020	Adopted - Complete
Hilton Road	03/08/2020	Adopted - Complete
Conington Road	14/08/2020	Adopted - Complete
Buckden Road	21/08/2020	Adopted - Complete
Potton Road	08/09/2020	Adopted - Complete
Woolley Road	11/09/2020	Adopted - Complete
Grafham Road	24/09/2020	Adopted - Complete
Mere Way	05/01/2021	Adopted - Complete
Ermine Street	Mar 2021	Adoption will be post Asphalt Batching plant removal
New Barns Lane	04/12/2020	Adopted - Complete

East

Adoption Package	Forecast / Actual *	Status
A14 Mainline	01/08/2019	Adopted - Complete
Swavesey Interchange	01/02/2021	Adopted - Complete
Bar Hill Interchange incl. Jug Handle	31/01/2021	Adopted - Complete
NMU routes across BN18	05/02/2021	Adopted - Complete
NMU routes across BN22	19/02/2021	#1 DOWL outanding
A1307 LAR – Dry Drayton Rd to Oakington road (across BE11)	22/12/2020	Adopted - Complete
A1307 LAR – Swavesey to Dry Drayton Road Roundabout (includes Oakington & Robins Lane)	22/12/2020	Adopted - Complete
A1307 LAR – Oakington Roundabout to Girton West Roundabout' #	22/12/2020	Adopted - Complete
A1307 LAR – Girton West Roundabout to Ch.+350	22/12/2020	Adopted - Complete
A1307 LAR – Girton West Ch.+350 to Huntingdon Rd	01/03/2021	Interim handover to HE Ops. CCC adoption following de-trunking
Histon Junction	Mar 2021	E/B offslip pedestrian crossing works to complete
Milton Junction	Mar 2021	White lining to complete

* Note – forecast adoption date includes CCC 28d notice

CCC Handover – Location of outstanding NMU & PROW

* Excludes PROW & some NMU Routes



Symbol Key re, adoption status

- NMU Open but not yet adopted
- NMU Not Constructed yet

Handover - Outstanding NMU & PROW

Package	Target	Status
Grafham Road NMU (from Grafham Road, across BN03)	Q2 2021	NMU Route Open – surface requires remedial works prior to CCC Adoption
Ermine Street NMU (to tie in within Wood Green Animal Sanctuary)	March 21	Construction of remaining NMU from Wood Green Animal Sanctuary to road side NMU
Fenstanton to Swavesey NMU (funded by Designated Funds)	March 21	Construction underway
Weavers Field	April 21	NMU Route Open – surface requires remedial works prior to CCC Adoption
Lolworth Footpath 5	Q2 2021	NMU Route Open – surface requires remedial works prior to CCC Adoption
Girton to Madingley to Huntingdon Road tie in	Q2 2021	Bridleway to be constructed on East side of A428
Mere Lane “The Boat” (Buckden Road)	Q2 2021	Footpath and PMA Open, requires adoption by CCC
