


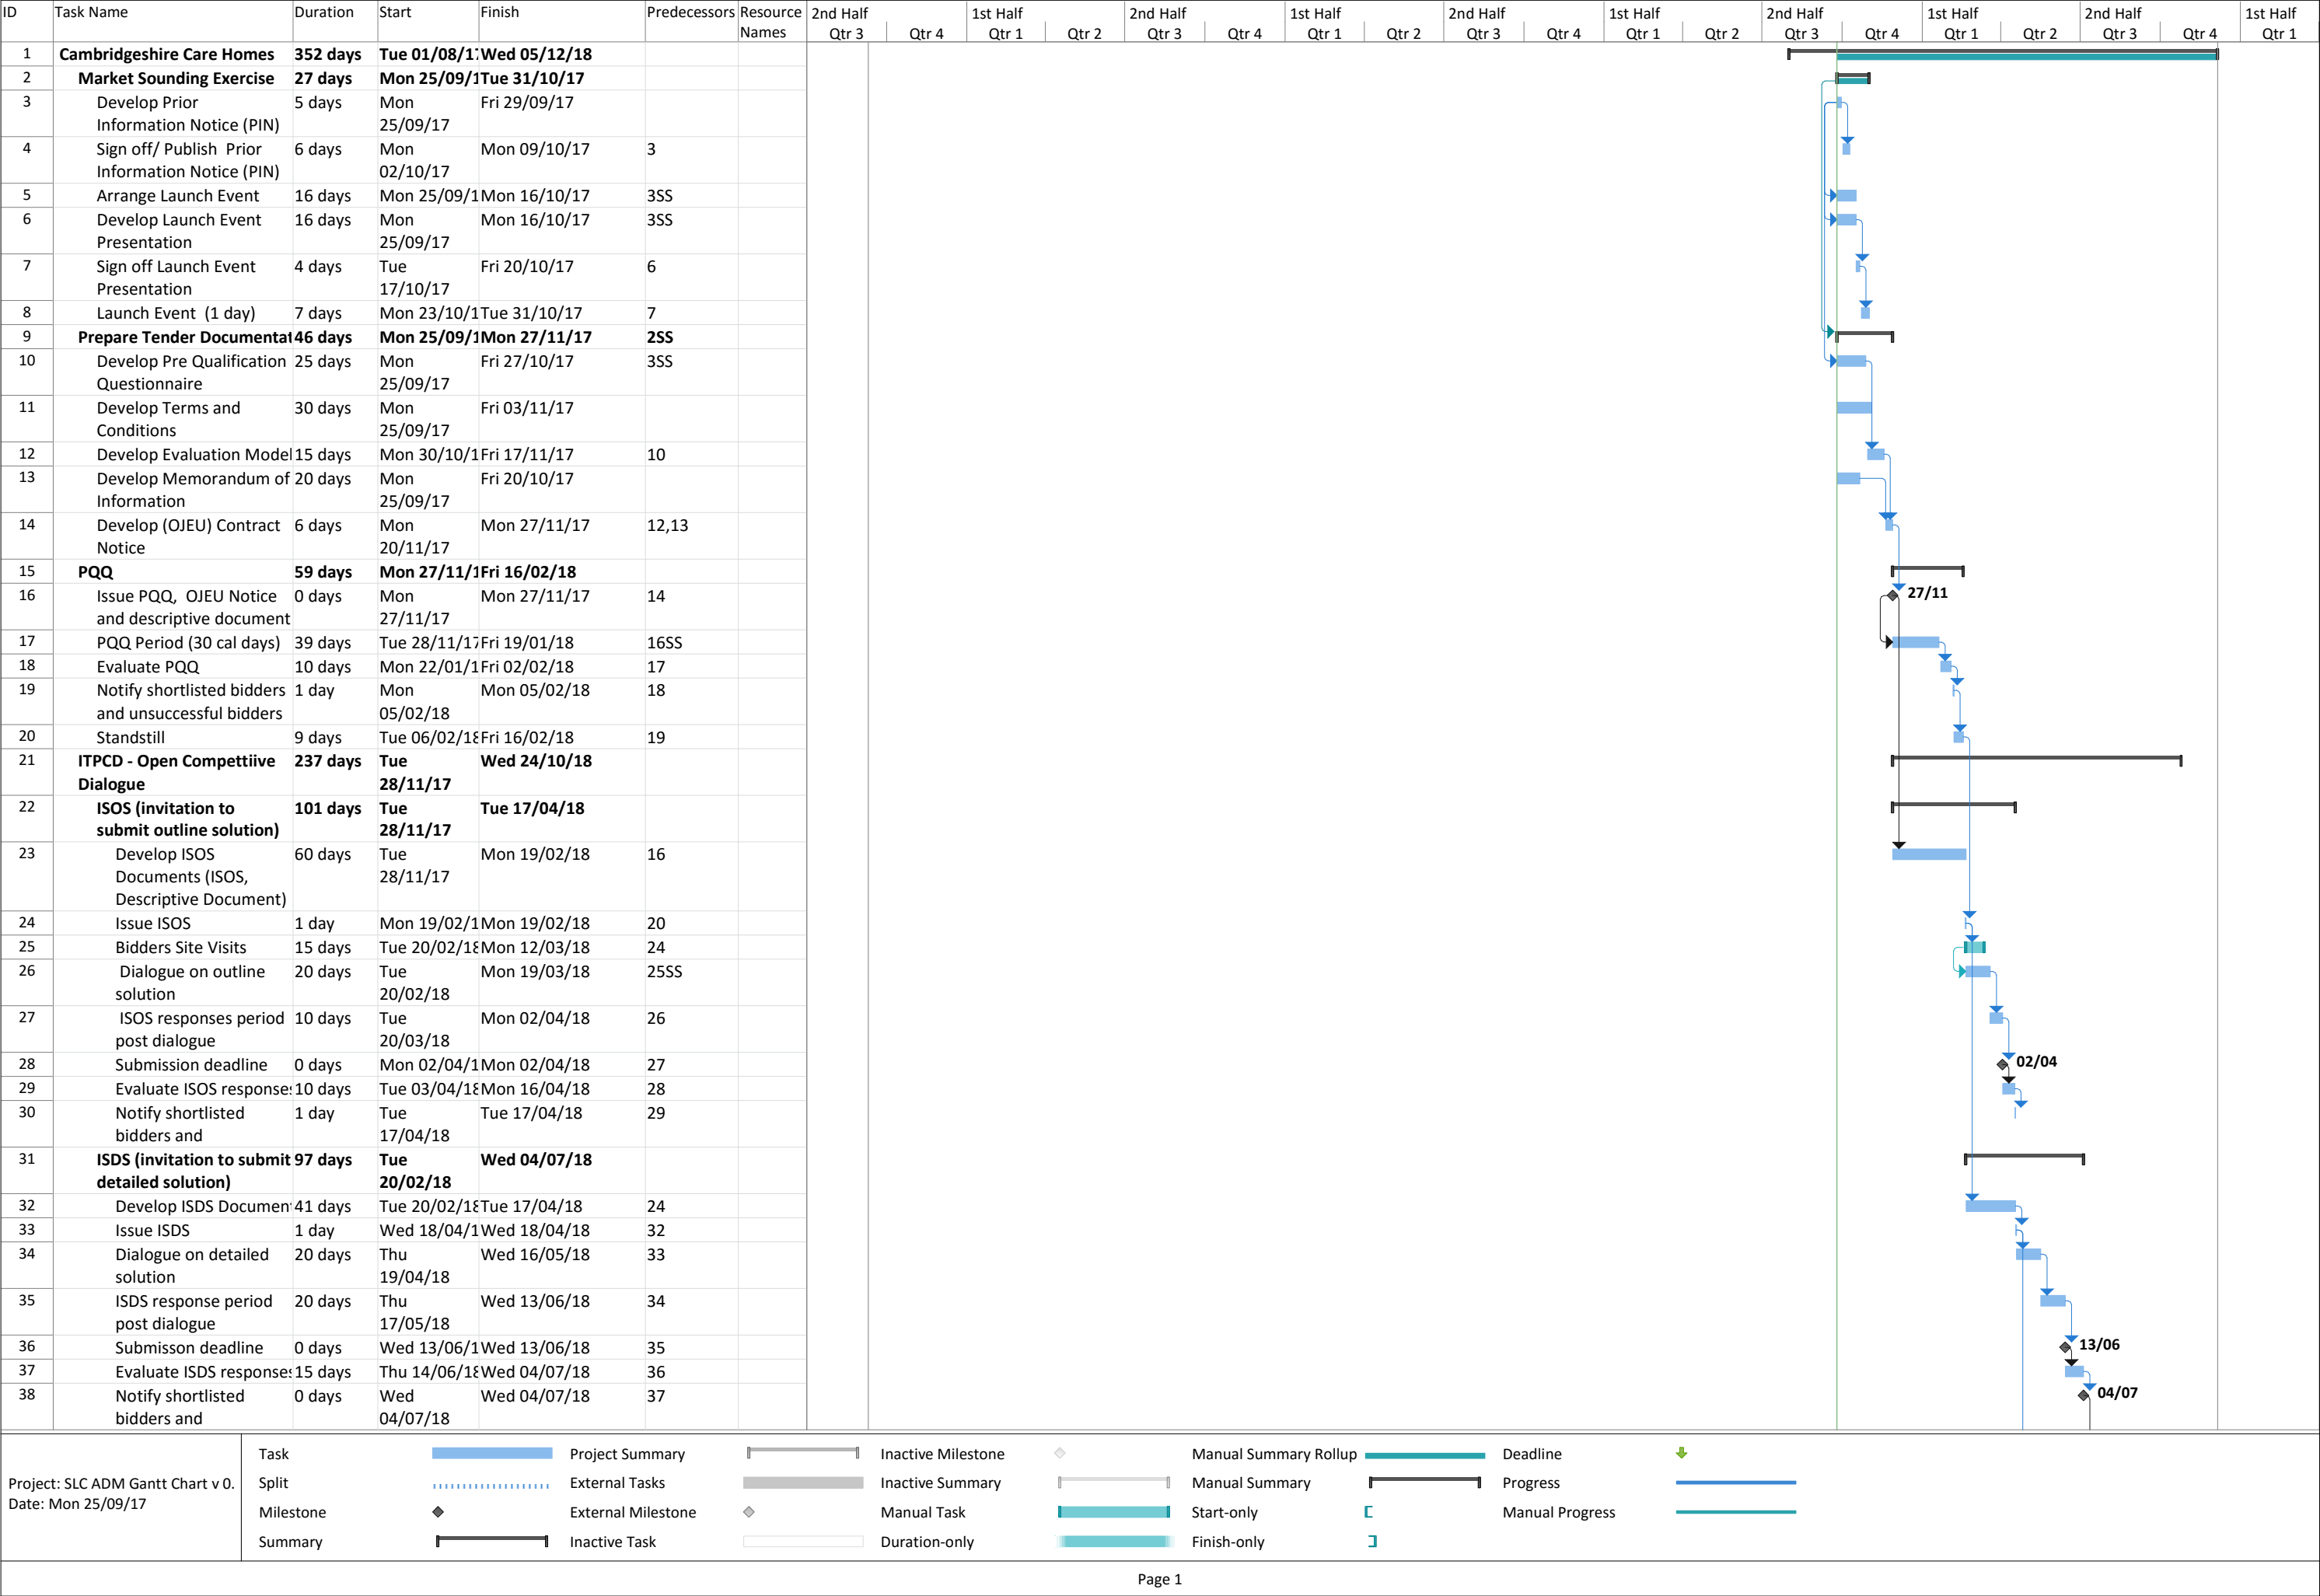

Page 1

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	2nd Half Qtr 3	Qtr 4	1st Half Qtr 1	Qtr 2	2nd Half Qtr 3	Qtr 4	1st Half Qtr 1	Qtr 2	2nd Half Qtr 3	Qtr 4	1st Half Qtr 1	Qtr 2	2nd Half Qtr 3	Qtr 4	1st Half Qtr 1	Qtr 2	2nd Half Qtr 3	Qtr 4	1st Half Qtr 1	
39	ISFT (invitation to submit final tender)	135 days	Thu 19/04/18	Wed 24/10/18																						
40	Develop ISFT Document	54 days	Thu 19/04/18	Tue 03/07/18	33																					
41	Issue ISFT	0 days	Wed 04/07/18	Wed 04/07/18	38																					
42	Dialogue on final solution	20 days	Thu 05/07/18	Wed 01/08/18	41																					
43	2nd dialogue session (LEGAL)	10 days	Thu 02/08/18	Wed 15/08/18	42																					
44	Legal Issued identified and clarified	10 days	Thu 16/08/18	Wed 29/08/18	43																					
45	3rd Dialogue / Site Visit	10 days	Thu 30/08/18	Wed 12/09/18	44																					
46	Close Dialogue	0 days	Wed 12/09/18	Wed 12/09/18	45																					
47	ISFT response period post dialogue	10 days	Thu 13/09/18	Wed 26/09/18	46																					
48	Submission deadline	0 days	Wed 26/09/18	Wed 26/09/18	47																					
49	Evaluate ISFT responses	10 days	Thu 27/09/18	Wed 10/10/18	48																					
50	Internal Approval Process for Preferred Bidder	10 days	Thu 11/10/18	Wed 24/10/18	49																					
51	Preferred Bidder	30 days	Thu 25/10/18	Wed 05/12/18	49																					
52	Post Tender contract negotiations	30 days	Thu 25/10/18	Wed 05/12/18	50																					

Project: SLC ADM Gantt Chart v 0.
Date: Mon 25/09/17

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

Manual Progress
